



Lower Otter Update Feb 22



Progress Since Dec 21

- Vegetation clearance has continued predominantly within Landfill area which has now been cleared to 300mm above ground level. Clearance between Big and Little bank now completed including area for the new footbridge in the south
- Fluming works to existing west trunk drain, fish rescue completed
- Installation of the piling mat at South Farm Road in preparation of the bridge construction works
- Cofferdam install completed for SRF bridge, this allows excavation of existing tip area and concrete works to be completed below water level.
- Import of material to build new SFR embankment being stockpiled on the existing Landfill Area






Progress Continued

- Excavation and removal of landfill material within cofferdam
- Completion of the pile mat for main Concrete Flight Auger Piling for SFR bridge
- Trial compaction of materials to be used within SFR embankment
- Installation of embankment monitoring stations
- Commencement of CFA piling for permanent piles SFR bridge



Program going forward March – May 22

- Early March will see the completion of permanent piles
- Excavation of the cofferdam to formation levels including breakdown of piles to required level
- Construction of pile caps to form the foundation of bridge and allow abutments and pier construction to the underside of the main bridge deck
- Commence excavation of southern creek from BSCC boundary to SFR bridge and Big bank to Little Bank
- Commence embankment construction utilising imported material, these works to the west and east of the new bridge
- Clearance of vegetation to ground Landfill area from April 22

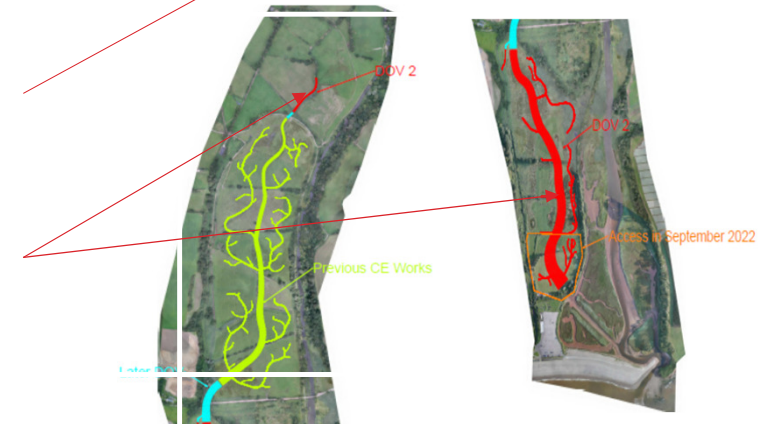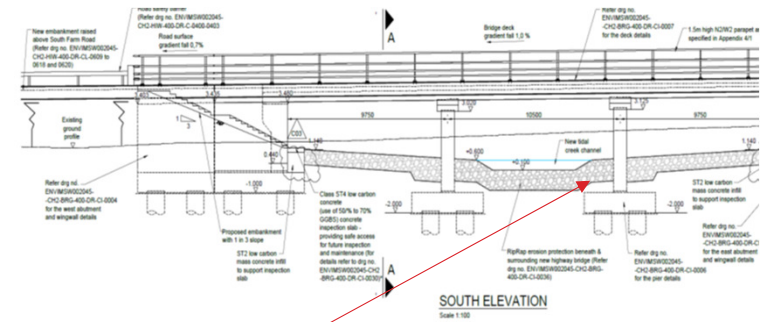

Public Liaison

- Launch of our new Face Book in February to provide another platform to update the community on the progress of the site please follow us <https://www.facebook.com/KIER-at-Lower-Otter-109330674991760/>
- Second edition of the Kier news will be published end March / early April providing an update of the works
- Vegetation clearance from footpath following storms



After storms Eunice & Franklin, work recommenced last week on the piled foundations for the new South Farm Road bridge, these piling works are planned to be complete by mid March.



Thank you

